## Columbus Avenue Parking-Protected Bicycle Path – Phase I (West 96<sup>th</sup> to West 86<sup>th</sup> Streets)

Implementation – Week 1 (Aug. 16 – Aug. 20, 2010)

 Contractor installed temporary markings for lane lines, "floating parking lane", channelization, mixing zones, and left-hand turn lanes between West 97<sup>th</sup> – West 86<sup>th</sup> Streets



Columbus Ave, facing south from West 97<sup>th</sup> Street

• Contractor installed thermoplastic markings over temporary markings for "floating parking lane" and striped buffer



Columbus Ave facing south towards West 88<sup>h</sup> Street



Columbus Ave, between West 97<sup>th</sup> and West 96<sup>th</sup> Streets

• Contractor installed green paint on bike path from West 96<sup>th</sup> Street to mid-block between West 87<sup>th</sup> and West 86<sup>th</sup> Street (relocated towed vehicle blocked completion of green paint installation)



Columbus Ave, facing north from West 90<sup>th</sup> Street



Columbus Ave, facing north towards West 87<sup>th</sup> Street

 Majority of vehicles parked in "floating parking lane" without being told, including delivery trucks; cyclists began using the facility almost as soon as yellow tape was removed



Columbus Ave, facing north between West 95<sup>th</sup> and West 94<sup>th</sup> Streets

 DOT installed MUNI Meters and No Stopping Anytime regulations for left-turn treatments; some segments being assessed to allow loading windows for deliveries and access-a-ride



Columbus Ave, facing south between West 91st and West 90th Streets

## Week 1 Summary:


- Channelization and left-turn only lane completed on Columbus Ave from West 97<sup>th</sup> West 96<sup>th</sup>
   Streets
- Floating parking lanes and buffers completed on Columbus Ave from West 96<sup>th</sup> West 86<sup>th</sup> Streets
- Mixing zones mostly completed on Columbus Ave from West 96<sup>th</sup> West 88<sup>th</sup> Street (yield teeth installation to commence Week 2)
- Left-turn only lane mostly completed on Columbus Ave at West 86<sup>th</sup> Street (installation of "ONLY" and left-turn arrow markings to be continued Week 2)
- Lane lines completed on Columbus Ave between West 97<sup>th</sup> and West 94<sup>th</sup> Streets (installation of lane lines and road wording "FIRE LANE" and "SCHOOL X-ING" to be continued Week 2)
- Green paint mostly completed on Columbus Ave from West 96<sup>th</sup> West 86<sup>th</sup> Streets (installation of segment between West 87<sup>th</sup> and West 86<sup>th</sup> Streets to be continued Week 2)
- Bike path/buffer divider line and intersection peg-a-track markings installation to be continued
   Week 2
- MUNI Meters installed between West 96<sup>th</sup> West 86<sup>th</sup> Streets
- 2-hour parking regulations and No Stopping Anytime regulations installed between West 96<sup>th</sup> and West 86<sup>th</sup> Streets
  - o Some parking regulations subject to change, based on loading needs as discussed above

## Week 2 Schedule:

- Continue installation of all thermoplastic markings, including lane lines and road wording, weather permitting
- Continue installation of green paint, weather permitting
- Finalize parking regulation changes

## Columbus Avenue Parking-Protected Bicycle Path West 96th - West 77th Streets - 2010

Phase I: Aug 16 - Oct 30\*

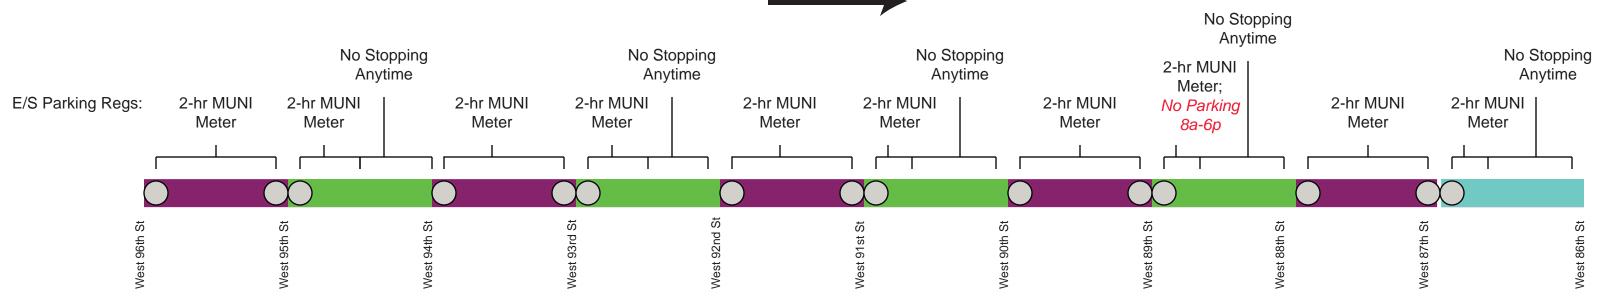

Phase II: Sep 13 (after resurfacing) - Nov 30\*

